blueplanet
a division of Ciena

FIXED FEE STATEMENT OF WORK

Customer Name:	BLUESTAR	**Quote Id #:**	Q-27738
Quote Requested By:	Fabio Pazolini	**SOW Author:**	John Smith

This Statement of Work ("SOW") is subject to, and incorporates by reference, the terms of the Blue Planet Professional Services Agreement, provided at Contract_link unless the parties have a fully executed Master Services Agreement which will govern (the "Agreement"). In case of a conflict between the terms of the Agreement and the terms of this SOW, the terms of this SOW will prevail.

Services	Fees	Expenses	Total Fees and Expenses
Fixed Fee Services	10,000$	100$	10,100$

All fees in this document are in US Dollars.

BlueStar Ltd		**Blue Planet Software, Inc.**	
Authorized Signature:	_____	**Authorized Signature:**	_____
Name:	_____	**Name:**	_____
Title:	_____	**Title:**	_____
Signature Date:	_____	**Signature Date:**	_____

DRAFT

FIXED FEE STATEMENT OF WORK

1. CUSTOMER OBLIGATIONS

Blue Planet's Fee for the performance of the services outlined in this Statement of Work is based upon the Customer's fulfillment (and its third parties, as applicable) of the obligations and upon the Project assumptions set out in this SOW. Blue Planet will not be responsible for any delays caused by, and Customer agrees to pay for any increased costs associated with, a Services deficiency to the extent it results from the Customer's failure to provide or meet the following:

A. Customer Obligations

A.1. Provide and maintain the properly sized and configured hardware, network, operating system, and database platform to perform the Services, in accordance with Blue Planet documented guidelines.

A.2. Obtain licenses for any necessary Blue Planet software programs before the commencement of Services, including any lab licenses which may be required by the customer over and above what is granted in the standard Blue Planet software license purchase.

A.3. Maintain Blue Planet Support entitlement for applicable Blue Planet software throughout the term of the Services.

A.4. Provide and maintain virtual private network (VPN) access to Customer systems through a network connection Customer creates between Blue Planet and its systems for the Blue Planet resources, including but not limited to, Blue Planet resources located onsite, remote and offshore.

A.5. Provide Blue Planet with full and timely access to office accommodations, facilities, equipment, applications and environments, complete and accurate information, correct and valid data from its systems, and relevant functional, technical, and business resources with skills and knowledge to document and approve Project requirements and to perform, test, and accept the Deliverables on a timely basis per the defined acceptance process.

A.6. Provide a safe and healthful workspace for Blue Planet resources performing on-site Services.

A.7. Provide notice to, obtain consents from, and facilitate and moderate interactions with third parties if specifically required for Blue Planet to perform Services.

A.8. Provide Blue Planet with access to production and shared development environments to the extent necessary for Blue Planet to perform Services.

A.9. Provide Blue Planet with a test environment that is Production-like in configuration for solution validation and User Acceptance Testing.

A.10. Lead and execute System Integration Testing to systems other than Project components.

A.11. Lead and execute User Acceptance Testing.

In the event that any unmet assumption or Customer responsibility delays or impairs the performance of the Services, then Blue Planet will not be liable for failure to perform its corresponding responsibilities unless the parties agree otherwise in writing. Further, to the extent of such delay or impairment, and without prejudice to its other rights and remedies, Blue Planet will be entitled to invoice, on a per daily basis, for additional time for performance of the Services.

DRAFT

blueplanet
a division of Ciena

FIXED FEE STATEMENT OF WORK

This Statement of Work is made up of the following Annexes:

- Annex A Commercial
- Annex B Services
- Annex C Implementation Deliverables

DRAFT

blueplanet
a division of Ciena

ANNEX A COMMERCIAL

2. DESCRIPTION OF SERVICES

Project Name (the "Project")	BlueStar BPO PS ENHANCEMENTS
Project Start Date	To be agreed by the Parties, but no earlier than 30 days from receipt of a valid purchase order and/or fully executed contract, as applicable
Project Type	Fixed Fee
Project Solution Type	Brownfield
Revision Date	<Submitted Version Date>

Blue Planet shall perform the Services as described herein and in Annex B ("Services" or "Project"). Services shall begin once a purchase order and/or executed contract is received on a date to be mutually agreed by the Parties, taking into account the Customer Obligations stated in Statement of Work, and shall be executed based on a continuous work schedule once started.

The Fees for the Project are based on the Scope of Work described in Annex B as well as the high-level project plan described in Annex C and shall utilize the Blue Planet Services Unified Method (BPSUM).

Changes to the Scope of Work, including any changes to the services to be performed, the resources required, the location of the resources where work is to be performed, the work schedule or execution methodology, or the high-level project plan shall be documented and approved by the Change Management Process.

3. PROJECT DELAY AND RESTART

If either Party deem that the Project shall be paused or delayed, the issue shall be handled as a Change Request to the Project as part of the Change Management Process. Any Change Request shall incorporate a 30 day minimum notification and wind down plan, after which time the Blue Planet project team shall be released from the Project in accordance with the Change Request.

The resumption of the Project shall be subject to an additional Change Request which shall outline the revised Project plan, timetable, and any applicable Fees. Blue Planet shall provide a timeline for the restart of the Project. Blue Planet shall resource the Project as required but does not guarantee that previous Project team members shall be members of the new Project team.

4. CHANGE MANAGEMENT PROCESS

If the Customer requests a change ("Change Request") to the project plans, scope, specifications, schedule, designs, requirements, service, deliverables, resource mix, software environment, or any other aspect of the Project, the Customer shall notify Blue Planet in writing (email shall suffice), specifying a description of the requested change and the reasons for the requested change. Upon receipt of such a request, and all relevant technical specifications and other necessary information, Blue Planet shall prepare a change request document giving an estimate of the costs associated with the requested change, including when applicable, making a feasibility study.

If Blue Planet requests a change, Blue Planet shall prepare a written Change Request, including the information as specified below, and submit the completed Change Request to the Customer.

Each Change Request shall describe the requested change with a reasonable level of details based on the facts and information known by Blue Planet at the relevant point of time and shall cover the following:

DRAFT

- A description of the requested change in relation to the scope of work as defined in the SOW and other relevant documents.
- An estimate of the impact of the requested change on the project time plan or the agreed Milestone Plan.
- Copies of, or reference to documents and correspondence in relation to the Change Requests and its origin including applicable names of Blue Planet and Customer resources responsible.
- The appliable Fee, or credit, for the requested change.

The Customer shall review the Change Request and shall, as soon as reasonably practicable after receipt of the Change Request, inform Blue Planet in writing of:

- Any clarifications required in relation to the Change Request; or
- such amendments as it reasonably determines should be made to the Change Request; or
- Its approval of the Change Request; or
- Its decision to take no further action in respect of the Change Request.

Delays in the Change Request approval process may affect the estimates provided with the Change Request.

Implementation of the Change Request is subject to execution of the formal Change Request document by both parties and, if applicable, issuance of any applicable purchase orders. Upon receipt thereof, Blue Planet shall incorporate the change(s) into the Project Plan and initiate change implementation.

If the Parties cannot agree on the Change Request, and Blue Planet or the Customer deem the Change Request necessary to the successful completion of the project, the proposed Change Request shall be reviewed by the Steering Committee.

5. ACCEPTANCE

Upon completion of a Blue Planet Milestone (as more specifically described in Annex C), Blue Planet shall issue an acceptance notice to Customer. Customer shall have five (5) business days ("Approval Period") to review the Milestone Deliverable(s). Before the end of the Approval Period, Customer shall provide to Blue Planet written notice of acceptance or non-acceptance of the Milestone Deliverable(s) with a list of any specific deficiencies, and each deficiency shall be prioritized in the response. Blue Planet shall address or correct the documented deficiencies before resubmitting the deliverable to Customer for further review. Upon resubmission Customer shall have a second Approval Period to review.

If Customer fail to deliver a written response confirming acceptance or non-acceptance within an Approval Period the Milestone and its Deliverable(s) shall be deemed accepted and invoicing for the Milestone shall commence upon the date of the written acceptance notice or deemed acceptance. If Blue Planet fails to deliver conforming Deliverable(s) during redelivery and/or the Customer rejects the Deliverable(s) after resubmission, then the parties shall escalate this through the escalation process as per the Project Governance.

If the Project is deployed to Customer's Production environment(s) prior to the acceptance of a Transition Phase Milestone then the Transition Phase Milestone, along with all previous Milestones, shall be deemed Accepted. If the Transition Milestone that has been deemed Accepted, then the Project shall move to Warranty and Support. **Blue Planet Software may not remain in a production environment beyond any test periods unless such Software is subject to a fully paid and valid license arrangement.**

DRAFT

ANNEX A COMMERCIAL

6. PAYMENT SCHEDULE

Customer agrees to pay Blue Planet the Fee pursuant to the terms of this SOW and the Agreement. The Fee is exclusive of (a) applicable taxes and (b) travel and out of pocket expenses, which will be mutually agreed and invoiced accordingly. Upon completion of a milestone, as described below, the corresponding milestone payment shall be invoiced and becomes noncancelable and nonrefundable. Milestones set forth below shall be deemed "complete" after Acceptance of all Deliverable within each applicable milestone.

Milestone	Milestone Description	Payment
1	Signing of Statement of Work	10%
2	Inception Phase Complete	15%
3	Elaboration Phase Complete	20%
4	Construction Phase Complete	40%
5	Transition Phase Complete	15%
	Total	**100%**

7. WORKING HOURS

Blue Planet resources are available Monday to Friday during normal local business hours, of the location in which the project resource resides, excluding holidays, and up to 8 hours a day from 8am to 5pm or as otherwise mutually agreed.

Blue Planet resources are not available to support Customer during the following times:

1. Vacation days. Blue Planet shall notify Customer with at least 3-weeks' notice of any upcoming vacation days.
2. Sick days and Statutory holidays, local and national, as per the location of the resource
3. Blue Planet training and conferences. Blue Planet shall notify Customer with as much notice as possible.

8. SUPPORT

If purchased, Solution Support will begin upon the acceptance of the final Deliverable pursuant to Acceptance in accordance with Section 4 above or when the project moves into production, whichever comes sooner.

DRAFT

ANNEX B SERVICES

1. SERVICES SCOPE

This Annex B Services describes the solution assumptions and constraints used to determine the Blue Planet professional services scope accompanying this Statement of Work. The solution assumptions and constraints quantify the solution configuration activities to be performed by Blue Planet.

The scope detailed in this Annex B provides the input to the planning, requirements, and detailed design of the project. Any changes to scope will be subject to change control. The technical details of how this scope will be delivered will be determined and documented in the design documentation [DS.140] of the Elaboration Phase.

1.1 PHASE 1

At the completion of this phase, BLUESTAR will be able to activate and terminate newly requested branded port resources, new service types and execute a custom operation for the purpose of ENNI and AEP port monitoring and reporting.

1.1.1 MAIN ASSUMPTIONS

The following lists the main assumptions supporting this Annex B.

1. Existing Magellan E-Access and Broadband service templates will be updated to support new branded port resources as part of this scope. No other changes will be made to other existing service templates.
2. For newly created services, MDSO will set the bandwidth and number of services thresholds on ENNIs. If required, BLUESTAR will have to perform this retrospective update manually for existing ENNIs.
3. Support of OAM Level 3 as per the standard current Magellan service templates.
4. No new branded ports will be created for NE's that do not support SC or MC-LAG ports as ENNI branded ports such as the TE.
5. The network service provisioning workflows shall be supported through MDSO GUI and Market APIs.
6. ENNI capacity threshold crossing will not block service provisioning and is only intended for reporting purposes.
7. The capacity threshold crossing will set a flag on the ENNI branded port. No alarm will be generated.
8. Reporting will be in JSON format through custom operation response. No PDF or CSV will be generated.
9. BLUESTAR to provide constraint profile for IDLs to be used in all service types.

DRAFT

ANNEX B SERVICES

1.1.2 BLUE PLANET ORCHESTRATION (BPO)

-Total of 2 new branded port resources to be implemented in MDSO:

- New ENNI Branded Port resource for SC-LAG and MC-LAG in MCP domain only.
- New ONNI Branded Port resource covering MCP, Skylight and Planet Operate domains. Can be SC-LAG, MC-LAG or Standard Ethernet Port.

-Total of 3 new service templates to be implemented in MDSO:

- New Magellan E-Transit service ENNI to ENNI
- New Magellan OFFNET service ENNI to ONNI
- New Broadband Plus service
- The new service templates will support the New LAG ENNI handoff ports

-Total of 3 existing service templates to be updated in MDSO:

- Magellan E-ACCESS EPL (to support the new ENNI SC-LAG and MC-LAG branded port)
- Magellan E-ACCESS EVPL (to support the new ENNI SC-LAG and MC-LAG branded port)
- Broadband (to support the new ENNI SC-LAG and MC-LAG branded port)

- Total of 1 custom operation to be implemented in MDSO on branded ENNI and AEP ports allowing for reporting of utilized bandwidth and number of services configured on the ENNI port. New visible flag will be introduced in the branded ports, the flag will be set upon crossing configurable thresholds for Utilized Bandwidth and Number of Services on ENNIs.

- The flag will be a new property on the applicable branded port resources.
- The flag will be a visible indicator that the ENNI set threshold was exceeded
- BLUESTAR can trigger the custom operation and consume the response via API.
- The response will be in JSON format detailing number of services, service id, customer, A port, Z Port, VLAN, profiles, Provisioned bandwidth.
- Reporting should be provided per ENNI and for all ENNIs. For All ENNIs, pagination will be required to iterate through large responses.

- A new ST Manager will be implemented that allows BLUESTAR to create a new top-level product with a title chosen by BLUESTAR e.g. Calypte Low Latency. This new top-level product will be called by the NB system to instantiate existing BLUESTAR branded services such as the Calypte EPL.

1.1.2.1 SERVICE INVENTORY

Service inventory will be accessible using the standard BPO UI.

DRAFT

1.1.2.1.1 DATA MIGRATION/SERVICE DISCOVERY

Service discovery and promotion is provided in the existing MDSO solution. The existing microservice will be enhanced to support promotion of network services for the service types defined in this document.

1.1.2.2 SERVICE ORCHESTRATION AND ACTIVATION (MDSO)

The following table lists the service template(s) to be updated in the solution.

Service Template	External API	Consumer	Lifecycle Operations	Additional Operations	Max Template Attributes
Magellan E-Access Service (EVPL)	*Market API*	*3rd Party*	*Activate/Update/Terminate*	*N/A*	*Same as existing templates*
Magellan E-Access Service (EPL)	*Market API*	*3rd Party*	*Activate/Update/Terminate*	*N/A*	*Same as existing templates*
Broadband	*Market API*	*3rd Party*	*Activate/Update/Terminate*	*N/A*	*Same as existing templates*

The following table lists the service template(s) to be created in the solution.

Service Template	External API	Consumer	Lifecycle Operations	Additional Operations	Max Template Attributes
Magellan E-Transit Service	*Market API*	*3rd Party*	*Activate/Update/Terminate*	*N/A*	*Same as existing templates*
OFFNET Magellan E-Transit Service	*Market API*	*3rd Party*	*Activate/Update/Terminate*	*N/A*	*Sames as existing templates*
Broadband Plus Service	*Market API*	*3rd Party*	*Activate/Update/Terminate*	*N/A*	*Sames as existing templates*
New ENNI SC-LAG and MC-LAG Branded Port Resources	*Market API*	*3rd Party*	*Activate/Update/Terminate*	*N/A*	*Additional attribute "lagType"*
New ONNI Branded Port Resource	*Market API*	*3rd Party*	*Activate/Update/Terminate*	*N/A*	*Additional attribute "lagType"*

ST Manager	*Market API*	*3rd Party*	*Create/Update/Terminate*	*N/A*	*No new attributes*

1.1.2.2.1 SERVICE ACTIVATION WORKFLOW

The following table lists the scope of each service template operation in the updated service templates.

Service Template	Operation	Network Domains/RA	Scope
Magellan E-Access Service(EVPL)	*Activate* *Terminate* *Update*	*MCP, Skylight, Planet Operate*	*Update existing service template to Activate/Terminate Magellan E-ACCESS services using new branded port resources (SC-LAG and MC-LAG) on MCP domain.*
Magellan E-Access Service(EPL)	*Activate* *Terminate* *Update*	*MCP, Skylight, Planet Operate*	*Update existing service template to Activate/Terminate Magellan E-ACCESS services using new branded port resources (SC-LAG and MC-LAG) on MCP domain.*
Broadband	*Activate* *Terminate* *Update*	*MCP, Calix, Planet Operate*	*Update existing service template to Activate/Terminate Broadband services new branded port resources (SC-LAG and MC-LAG) on MCP domain.*

The following table lists the scope of each service template operation in the new service templates.

Service Template	Operation	Network Domains/RA	Scope
Magellan E-Transit Service	*Activate* *Terminate* *Update*	*MCP, Skylight, Planet Operate*	*New service template to Activate/Terminate Magellan E-Transit services ENNI to ENNI. Endpoints can be on MCP (Standard Ethernet, new SC-LAG and MC-LAG), Skylight (SC-LAG and Standard Ethernet), Planet Operate (Standard Ethernet). Prefix is set to CET. This service requires a VLAN ID (numeric number) and VLAN Ethertype (S-VLAN **88a8** or C-VLAN **8100**) on both ends.*
OFFNET Magellan	*Activate*	*MCP, Skylight, Planet Operate*	*New service template to Activate/Terminate OFFNET*

ANNEX B SERVICES

E-Transit Service	*Terminate* *Update*		*Magellan E-Transit services ENNI to ONNI. Endpoints can be on MCP (Standard Ethernet, SC-LAG and MC-LAG), Skylight (SC-LAG and Standard Ethernet), Planet Operate (Standard Ethernet). Prefix: TBD by BLUESTAR*
Broadband Plus Service	*Activate* *Terminate* *Update*	*MCP, Calix*	*New service template to Activate/Terminate Broadband Plus services. COS value will be set to 2. Endpoints can be on MCP (Standard Ethernet, SC-LAG and MC-LAG), Calix (ONT Port). Should have a different constraint profile to use a separate dedicated IDL. Prefix: GEP*
New ENNI SC-LAG and MC-LAG Branded Port Resources	*Activate* *Terminate* *Update*	*MCP*	*New ENNI Branded Port resource for SC-LAG or MC-LAG on MCP.*
New ONNI Branded Port Resource	*Activate* *Terminate* *Update*	*MCP, Skylight, Planet Operate*	*New ENNI Branded Port resource which:* *Can be SC-LAG, MC-LAG or Standard Ethernet port on MCP.* *Can be SC-LAG or Standard Ethernet port on Skylight.* *Can be Standard Ethernet on PO.* *The ONNI need to be a Separate Branded Port Resource as the customer's name will always be BLUESTAR.*
ENNI and AEP ports capacity Monitoring and Reporting	*Custom Operation*	*MCP, Skylight, Planet Operate*	*Custom operation to report utilized bandwidth PER ENNI. Allow to set KPIs on ENNI for Number of services provisioned on ENNI and utilized bandwidth (SUM of CIR). Threshold TBD by BLUESTAR as a configurable percentage for utilized bandwidth and as a configurable number for number of services. Report to be in JSON format. All provisioned and promoted*

DRAFT

			services should include the KPIs for reporting and monitoring. Magellan ENNI, LAG ENNI, ONNI and Calypte EVPL ENNI.
ST Manager	*Create/Update/Terminate*	*Internal*	*New top-level product that instantiates existing BLUESTAR branded service types. No change to existing resource types. Update allows modification of product title. Terminate is only possible if no resources are instantiated under this product.*

Additional business use cases not directly addressed by the above service template workflows will be the responsibility of the northbound system to orchestrate using the available service templates and operations – Activate, Terminate, Update – to achieve the desired outcome.

DRAFT

1.1.2.2.2 SERVICE ACTIVATION INTERFACES

Other than the Network Provisioning interfaces supporting the service templates, there are no additional interfaces to the ecosystem.

1.1.2.2.3 INTERNAL RESOURCE PROVIDERS

VLAN tags to be allocated from existing VLAN pool.

1.1.2.2.4 TESTING AUTOMATION

Postman collections for automation of regression testing of the following Workflows.

Applicable Service Activate, Termination, Update Workflows:

1- Calypte (EPL, EVPL)
2- Magellan EPL
3- Magellan E-ACCESS (EPL, EVPL)
4- Magellan E-Transit
5- OFFNET Magellan E-Transit
6- Broadband
7- Broadband Plus

Applicable branded ports:

1- Calypte EPL, EVPL
2- Magellan EPL
3- Magellan ENNI, ENNI LAG, ONNI
4- Broadband ONT port

1.1.2.2.5 NETWORK PROVISIONING

The following sections list the Resource Adapters and Domains required to support the service activation workflows.

Network Vendor Domain	**Calix CMS**
Equipment Models	No change to existing product RA
Card Models	No change to existing product RA
Management System	NMS
Interface Spec.	Support setting COS 2 value for Broadband Plus services.
Type	No change to existing product RA
Version	16.0.0.4
Is Product RA	Yes – Licensed Product

DRAFT

ANNEX B SERVICES

Model	No change to existing product RA
Use case	Service Provisioning and Discovery

Network Vendor Domain	**Ciena NCS**
Equipment Models	No change to existing product RA
Card Models	No change to existing product RA
Management System	NMS
Interface Spec.	No change to existing product RA
Type	No change to existing product RA
Version	NCS 10.0
Is Product RA	Yes – Licensed Product
Model	No change to existing product RA
Use case	Service Provisioning and Discovery

Network Vendor Domain	**Skylight**
Equipment Models	No change to existing product RA
Card Models	No change to existing product RA
Management System	*NMS*
Interface Spec.	No change to existing product RA.
Type	No change to existing product RA
Version	23.12.1 GA 15 949638b
Is Product RA	*Yes*
Model	No change to existing product RA
Use case	Service Provisioning and Discovery

DRAFT

ANNEX B SERVICES

Network Vendor Domain	Planet Operate
Equipment Models	No change to existing product RA
Card Models	No change to existing product RA
Management System	*NMS*
Interface Spec.	No change to existing product RA
Type	No change to existing product RA
Version	17.08.06.-37005
Is Product RA	*Yes*
Model	No change to existing product RA
Use case	Service Provisioning and Discovery

DRAFT

ANNEX B SERVICES

DRAFT

ANNEX C IMPLEMENTATION DELIVERABLES

1. INTRODUCTION

This Annex C describes the approach to delivery of the Project including the methodology, key tasks and deliverables to be performed by Blue Planet and Customer.

2. PROJECT DELIVERY METHODOLOGY

Blue Planet use BPSUM+, a proven standards-based method that enables and supports the full project lifecycle. It is built on the Project Management Institute's Project Management Body of Knowledge (PMBOK) Global Standard.

BPSUM+ Provides an implementation approach that is flexible, scalable, adaptable, rapid, business and risk focused, which supports all software development and implementation approaches including Agile, Scrum, Waterfall, and Cloud.

3. PROJECT IMPLEMENTATION TIMELINE

The general elements of the project timeline are as follows:

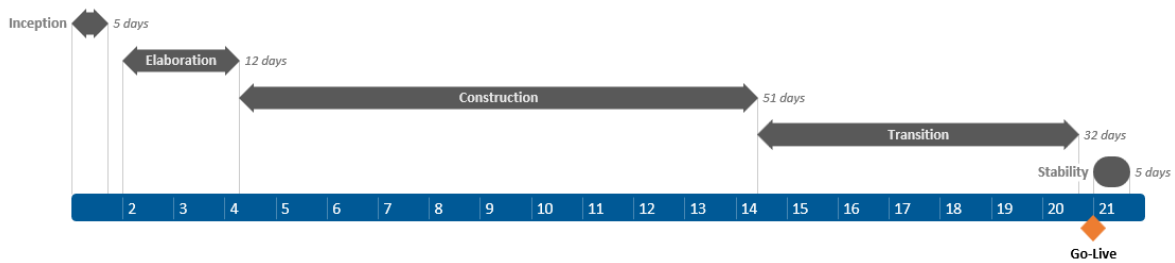

This timeline shall be refined and confirmed at the end of the Inception and Elaboration phases of the Project.

The Project will be delivered in the following four BPSUM phases:

A. **Inception Phase**

Pre-Requisites to the initiation of Inception Phase:

1. Project kick-off between Blue Planet and Customer, including Project stakeholders and sponsors.
2. Review of Customer Obligations and timeframe for completion.

Services and Deliverables:

1. Conduct a Governance Workshop with the Customer's Project Manager to align on the following type of project management items:
    - A.1.1. Related Invoicing Milestones
    - A.1.2. Storage of project **artefacts** (Action, Risk Register)
    - A.1.3. Cadence and logistics of Project Meetings, Status updates etc.
    - A.1.4. Change Management Procedures
    - A.1.5. RACI
    - A.1.6. Agreed use of tooling to enable the Project delivery.

2. Define a preliminary Project Schedule with phase duration and dependencies.
3. Conduct a Requirements Workshop, with Customer's designated subject matter experts, for a period not to exceed 6 days. This is to capture and validate the requirements of functional scope, operational scope and architecture validating the scope captured in Annex B. We will identify any changes to scope, which will be managed via the change control process, and identify any gaps. The deliverable from the workshop will be a Requirements Specification document (RD.140) which will consist of a consolidated list of functional and other operational requirements, and an architecture description which identifies the system's architecture.

The Requirements Specification documentation, which includes the Requirement Traceability Matrix, is the 'Inception Phase Deliverable' (RD.140).

B. **Elaboration Phase**

Pre-Requisite to the initiation of Elaboration Phase:
1. Acceptance of Inception Phase Deliverables

Services and Deliverables:

1. Assist Customer with the install and/or setup of one (1) development environment for the Project.
2. Blue Planet will deliver a detailed Project Schedule (BT.070), which will consist of an agreed Project Workplan with tasks, task start and end dates and task durations, and dependencies. This plan will include any planned Showcases / Demos of the solution during the construction phase.
3. Blue Planet will deliver a Design Specification document (DS.140) which will include a High Level Design and provides input into the implementation of the system as designed.
4. Blue Planet will deliver a Test Strategy document (TS.100) document with an agreed approach to Testing, Phases and Outcomes included.

The Project Detailed Schedule (BT.070), Design Specification (DS.140) and Test Strategy (TS.100) are the 'Elaboration Phase Deliverables'.

C. **Construction Phase**

Pre-Requisite to the Initiation of Construction Phase
1. Acceptance of the Elaboration Phase Deliverables.
2. Blue Planet development environment is available in Customer's lab or network.

Services and Deliverables:

1. Implementation of the agreed Requirements and Design in Customer's lab environment.
2. System and Systems Integration Test Results (TE.100), with an indication of pass/fail for each test scenario, along with a list of applicable open issues.
3. Prepare a User Guide (DO.070) to assist Customer with using the specific solution, this is to complement the Product User Guide.

The System and Systems Integration Test Results (TE.100) and the User Guide documentation (DO.070) are the

DRAFT

'Construction Phase Deliverables'. The TE.100 will contain the acceptance criteria by severity of issues.

D. **Transition Phase**

Pre-Requisite for the initiation of Transition Phase

1. Acceptance of Construction Phase Deliverables
2. A Blue Planet environment for User Acceptance Testing is available and configured in the Customer's lab and preprod or network.
3. The Customer has documented the User Acceptance Test (UAT) cases to be executed.
4. The Customer and Blue Planet have reviewed and Accepted the UAT cases.

Services and Deliverables:

1. Deploy the System and Systems Integration Tested Services into Customer's Test environment as required.
2. Provide up to twenty (20) days to assist with Customer's User Acceptance Testing in the lab and preprod environment.
3. Customer to approve the successful acceptance testing (UAT) exit criteria. The TE.100 contains the acceptance criteria by severity of issues.

The key outcome from the Transition Phase is acceptance of the User Acceptance Testing (UAT).

4. SUMMARY OF PROJECT DELIVERABLES

Customer acceptance is expected against the Project deliverables within 5 working days. The commencement of the subsequent phase or activity is dependent on the successful acceptance of the applicable deliverable.

Phase	Deliverable
Inception	Requirements Specification documentation (RD.140)
Elaboration	Updated Project Detailed Schedule (BT.070)
Elaboration	Design Specification (DS.140)
Elaboration	Test Strategy (TS.100)
Construction	System and Systems Integration Test Results (TE.100)
Construction	User Guide documentation (DO.070)
Transition	Support User Acceptance Testing (UAT)

DRAFT

ANNEX C IMPLEMENTATION DELIVERABLES

5. PROJECT ENVIRONMENTS

Blue Planet requires a minimal set of project environments within the Customer's environment. Typical project environments include, but are not limited to:

1. Development
2. Quality Assurance
3. User Acceptance Test
4. Staging/Pre-Production
5. Production

The minimum set of environments are 1) Development 2) Quality Assurance and 5) Production.

Non-production environments shall be connected to all systems, application APIs, lab equipment, and other resources required for Blue Planet to develop the Project. Each environment shall be connected to different systems as required. For example, the Blue Planet Development environment shall not be connected to the same Ticketing system as the Blue Planet UAT environment, but the two environments can be connected to the same Active Directory/LDAP systems.

Separate QA and UAT environments allow the two different user groups, Quality Assurance and User Testing, to continue their respective testing without impacting the other during the Project lifecycle, with respect to data, data loads, software issues, and solution deployments.

The Staging/Pre-production environment(s) provide Blue Planet the ability to deploy the solution to production-like environment to ensure the successful Production deployment(s). Staging/Pre-production environments include all Production services including, but not limited to, similar hardware sizing, load balancing architecture, high availability, georedundancy, and LDAP/SSO. The Staging environment(s) also provide an environment for the investigation of Production issues. In addition to the platform being configured in the same way as Production, the data and data quality must also be like Production.

5.1 PROJECT DEVELOPMENT IN PRODUCTION ENVIRONMENT

All Blue Planet development and testing in the Customer's environment shall be done within those Customer-provided Development, Test/QA, and Staging environments. If the Blue Planet Development or Test/QA environments shall be required to connect or interface, in any capacity, to Customer's Production network or system environment(s), Customer shall promptly authorize such connection. Customer authorization shall be given to Blue Planet either a) explicitly by email or b) implicitly by Customer providing resource details, credentials, or any other details needed for Blue Planet to connect to the Production network environment or systems prior.

As a result of the Customer's authorization, Blue Planet shall not be responsible and liable for any loss of service, data loss or corruption, system failure or corruption, or hardware failures in the Production environment(s) due to the Project development and testing in the Production environment(s). Blue Planet Software may not remain in a production environment beyond any test periods unless such Software is subject to a fully paid and valid license arrangement.

DRAFT

ANNEX C IMPLEMENTATION DELIVERABLES

6. PROJECT MANAGEMENT

The Parties agree to designate a project manager that shall work together to facilitate an efficient delivery of the Project.

The Project Management team is comprised of the following resources:

The Blue Planet Project Manager, who will:

1. Manage the Blue Planet project and be the main point of contact for Blue Planet deliverables and resourcing.
2. Manage and schedule the engage of Blue Planet resources in the delivery of the Project.

The Blue Planet Project Manager is not responsible for the engagement, scheduling, and overall management of the Customer teams, resources, systems, SMEs, etc.

The Customer Project Manager(s), who will:

1. Manage the Project on behalf of the Customer and be the main point of contact for the Blue Planet project manager.
2. Manage and promptly schedule the engagement of its resources (e.g. network resources, IT teams, SMEs, systems, procurement) in the delivery of the Project.
3. Manage and deliver the defined deliverables as per the Project plan document.
4. Define, manage, track, and resolve Customer issues as per the Project RAID document in a timely manner.
5. Manage and facilitate engagements, deliverables, and issue tracking with its teams and external vendors, if applicable, to deliver the Project.
6. Provide the required Acceptance for Blue Planet Deliverables in accordance with this SOW.

6.1 RACI

The roles and responsibilities matrix below show the breakout of the tasks and deliverables for the Project with the responsibility for the tasks and deliverables as either being that of Responsible, Accountable, Consulted, Informed (RACI).

Responsible: Who is responsible for carrying out the task

Accountable: The one ultimately answerable for the correct and thorough completion of the deliverable or task, the one who ensures the prerequisites of the task are met and who delegates the work to those responsible.

Consulted: Those whose opinions are sought, typically subject matter experts, who can provide valuable advice or consultation for the task

Informed: Those who are kept up to date on progress, often only on completion of the task or deliverable.

DRAFT

ANNEX C IMPLEMENTATION DELIVERABLES

	Customer	Blue Planet
Project Management		
Creation and management of overall project schedule and sprint contents	A	R
Assignment and resolution of Blue Planet Tasks, Issues, Actions	C	R, A
Assignment and resolution of Customer Tasks, Issues, Actions	R, A	C
Schedule of project meetings, creation of project minutes, email updates, and status document	C	R, A
Schedule of any resource(s) necessary for project meetings, required for Blue Planet to complete the Project and Deliverables	R, A	C
Schedule and Running of Go/No Go Meetings for Releases	R	A
Decision for Production Go/No Go	A	C
Management and scheduling of all Customer resources, systems, and deliverables	R, A	C
Management of the Project RAID document	C	R, A
Inception Phase		
Project Kick-off meeting including review of high-level timeline and dependencies	C	R, A
Conduct SOW Review with Project Leaders and stakeholders	C	R, A
Conduct Governance Meeting and Review	C	R, A
Create requirements agenda and schedule the sessions. Identify and schedule required Customer SMEs to participate such that Blue Planet can complete the Inception Deliverables	R, A	C
Provide all materials and resources required by Blue Planet required to complete Inception Phase	R, A	C
Delivery of Requirements Specification RD.140 to Customer	C	R, A

DRAFT

ANNEX C IMPLEMENTATION DELIVERABLES

Elaboration Phase		
Provide Blue Planet platform and installation documentation to Customer	C	R, A
Acquire, install, and configure required network resources and systems needed for Blue Planet software install	R, A	C
Installation of Blue Planet software on Customer resources for Development and Testing	C	R, A
Create and schedule the Design sessions agenda, identify, and schedule Customer SMEs to participate such that Blue Planet can complete the Elaboration Deliverables	R, A	C
Provide all materials and resources required by Blue Planet required to complete Elaboration Phase	R, A	C
Definition of all naming conventions required by the Project including physical equipment, services, numbering, number ranges, and order numbers.	R, A	C
Delivery of BT.070 Project Management Detailed Schedule to Customer	C	R, A
Delivery of Design Specification DS.140 to Customer	C	R, A
Construction Phase		
Deliver the Project configuration outlined in this SOW	C	R, A
Configuration of Blue Planet software as outlined in this SOW	C	R, A
Co-ordinate and manage all Customer systems, resources, data ETL, vendor applications and systems, network resources, and connectivity required for Blue Planet to construct the solution.	R, A	C
Co-ordinate and manage all non-Blue Planet application and systems deliverables and timelines that are required for the Construction phase required by Blue Planet to meet the Project timelines	R, A	C
Provide and manage Virtual Private Network (VPN) or remote access for the whole Blue Planet project team, in a timely manner, such that solution development can occur remotely and from multiple global regions.	R, A	C

DRAFT

Schedule solution sessions between Blue Planet and Customer to resolve solution design, systems integration, data quality, or any solution issue that requires resolution	C	R, A
Schedule, participate and attend solution sessions required to resolve issues in a timely manner, including external vendor participants.	R, A	C
Delivery of Systems Integration Test Results document (TE.100)	C	R, A
Create the User Acceptance Test (UAT) document that shall be used by Customer to complete the Transition Phase.	R, A	C
Review and Accept the User Acceptance Test document from Customer	C	R, A
Resolve any issues identified by Blue Planet prior to Acceptance of UAT document	R, A	C
Transition Phase		
Lead and execution of User Acceptance Testing, by Customer resources, defined by the UAT Document approved in the Construction Phase.	R, A	C
Manage and co-ordinate all non-Blue Planet systems and activities, issues and actions required for the execution of User Acceptance Testing	R, A	C
Document, review, and track all issues related to Blue Planet required for Acceptance	R, A	C
Review and Acceptance of User Acceptance Test Cases and results by Customer	R, A	C
Support Customer resource's executing test cases in the identification of Blue Planet issues or errors	R	A
Manage and resolve all Blue Planet issues and actions found during the Transition Phase	C	R, A
Solution Environment and Maintenance		
All Hardware and Software procurement, configuration and setup of all Customer infrastructure and resources for the installation of Blue Planet software on the agreed Project environments.	R, A	C
Configuration of load balancers, firewalls, access control lists (ACL), application credentials, and non-Blue Planet systems	R, A	C

DRAFT

Blue Planet Software installation, as per this SOW	C	R, A
Blue Planet Software – log warranty and product support cases and monitor resolution	I	R
External Systems Integration		
Provide vendor documentation including API documentation, whitepapers, solution architecture, best practices, or other that are required by Blue Planet for the Project	R, A	C
Manage the third-party relationship for integrations	R,A	C
Co-ordinate and manage interactions, meetings, documentation, and approvals between Blue Planet and external systems owners or vendors.	R, A	C
Co-ordinate and manage all access and credentials required by Blue Planet needed to integrate with external systems required as part of the Project.	R, A	C
Blue Planet shall aid Customer IT or relevant team in the deployment and configuration of the services to Customer Production environment after completion of Transition Phase(s)	A, C	R
Data Migration – Extract, Transform, Load		
Identification of data sources including documenting the complete data sets for migration to Blue Planet.	R, A	C
Extract and clean data from migration data source(s) into an agreed format required by the Blue Planet solution data model.	R, A	C
Clean data extraction includes identifying the primary source of entity details, resolution of duplicate data or redundancy, missing data, resolving non-unique data, attribute mappings, etc. as required for Blue Planet to load high quality data to the Solution	R, A	C
Data transformation of all extracted data that conforms to the solution data model, naming conventions, data uniqueness requirements	R, A	C
Load the extracted and clean data into Blue Planet environment(s) required by the Project	C	R, A
Provide reports and metrics on Data Load executions	C	R, A

DRAFT

Validation of migrated data in test and production environments	R, C	A

7. PROJECT GOVERNANCE

The Parties agree to the proposed Project Governance structure described below with respect to project issues, escalation, and resolution decision-making.

7.1 GOVERNANCE STRUCTURES

7.1.1 STEERING COMMITTEE

The Steering Committee is the highest management body for the Project, consisting of Customer and Blue Planet senior management and key business stakeholders. Its key responsibilities are:

1. To validate progress and ensure the Project is operating in accordance with the obligations set out in this SOW.
2. To make decisions on the Project, including any necessary changes to the SOW such as scope of work, schedules (including milestones and deadlines if applicable), and Fees.
3. To address risks or issues escalated by the Project Program Board (as defined below).

7.1.2 PROGRAM BOARD

The Project Program Board sits between the Steering Committee (as defined above) and the Project Management Team (as defined below) and consists of the Partys' program directors and management.

The Program Board's key responsibilities include:

- Providing a point of escalation and a decision-making alternative for the Project.
- Serving as the management Team, thus minimizing the need to escalate issues to the Steering Committee.
- Filter and validating the flow of escalations to the Steering Committee to ensure that issues raised to that level are relevant and appropriate.
- Oversee the performance of the Project Management Team (as defined below) in terms of its day-to-day operation.

7.1.3 PROJECT MANAGEMENT TEAM

The Project Management Team is responsible for day-to-day Project management and owns all operational level activities required for the successful delivery of the Project. The Project Management Team is comprised of, but not limited to, a Project Manager from Blue Planet and a Project Manager from Customer.

The Project Management Team's key responsibilities include:

- The realization of, and adherence to, the SOW terms.
- Ownership of day-to-day project management activities.

DRAFT

- Unless otherwise stipulated, making all decisions necessary to ensure the adherence to schedules, budgets and agreed levels of quality.
- Delegation of authority to team leaders and other team members as appropriate.

7.1.4 ESCALATION PROCEDURE

If a joint decision cannot be made on any issue related to the fulfilment of the SOW, or if any dispute arises, the following escalation procedure shall apply:

9. First level of escalation – Project Management Team
   - If there is a disagreement between the stakeholders which cannot be resolved at the operational level, the issue shall be escalated to the Project Management Team.
   - The Project Management Team shall record the issue in the appropriate issue log.
   - The issue shall then be owned by the Program Management Team.
   - If the Program Management Team resolve the issue, the decision shall be recorded in the appropriate log and the project teams are provided with the instruction necessary to fulfil the terms of this SOW.
   - If the Management Team cannot resolve the issue, it shall be escalated to the Project Board.

10. Second level of escalation – Project Board
    - The Project Management Team shall update the issue log to reflect this 2nd level escalation.
    - If the issue is resolved at this level, the decision shall be recorded, and the project team provided with the appropriate instruction.
    - If the issue cannot be resolved, the Project Board shall promptly escalate the issue to the Steering Committee in writing (email shall suffice).

11. Third level of escalation – Steering Committee
    - The Steering Committee shall determine a resolution on the escalated issue as it deems appropriate.
    - Until such time as the decision is made in the escalation procedure, the stakeholders shall continue to execute the contract in good faith.
    - The Project Management Team shall update the logs accordingly to reflect the decision and/or outcome from the Steering Committee.

END OF DOCUMENT

DRAFT
